

South Granville Water And Sewer Authority

Executive Director's Monthly Project Update Report

July 2026

To: SGWASA Board Members

From: Scott N. Schroyer, Executive Director *SNS*

Topic: Topics Update Report for July 2026

Date: Report Issue Date 8/6/2026

Executive Summary

This monthly report provides the Board with a concise status update on SGWASA's major capital projects, regulatory compliance activities, and utility operations for July 2026. Overall, SGWASA's major projects remain active and generally on schedule, with several key milestones reached during the month and several upcoming items requiring continued monitoring.

- **PFAS Mitigation:** The PFAS Advanced Water Treatment project reached the 60% design milestone on June 23, and the 90% design package is scheduled for September 2026. The AquaPRS pilot unit was delivered on July 31, with startup and commissioning planned for August. SGWASA also received \$260,472.08 in July from the AFFF PFAS Multi-District Settlement.
- **I-85 Sewer Improvements:** Construction Package #1 and Construction Package #2 remain in progress, on schedule, and within budget. July work included sewer pipe installation, pump station construction activities, railroad crossing preparation, and directional bore work under NC Hwy. 85.
- **Water Meter Replacement:** The Creedmoor service area meter replacement project is approximately 70% complete, with the revised completion target remaining December 1, 2026.
- **Water Treatment and Distribution Planning:** The filter media replacement project is complete and is showing improved filter run times, lower turbidity, and reduced ferric usage. The AIA water and wastewater assessment final draft reports were reviewed in July, with final reports expected in August.
- **Water Quality Improvements:** Hazen & Sawyer continues work on hydraulic modeling, flushing program development, booster station assessments, and distribution control evaluations. The unidirectional hydrant flushing pilot remains on hold due to weather and drought conditions, with a tentative mid-to-late September start based on Lake Holt levels.
- **Operations and Staffing:** No significant utility operations issues were reported for July. Staffing remains above 94% of the FY26-27 authorized level, with one Billing Customer Service Supervisor vacancy currently being advertised or interviewed.

South Granville Water And Sewer Authority

Executive Director's Monthly Project Update Report

July 2026

Board Status Summary

Project / Program	Status	June Update	Board Attention
PFAS Mitigation	● On Schedule	60% AWT design completed June 23; 90% design is scheduled for September 2026; AquaPRS pilot unit delivered July 31 with startup planned in August; AFFF settlement funding of \$260,472.08 received in July.	Monitor 90% design review, Butner permitting, USDA application, pilot startup, and any additional PFAS settlement funding.
I-85 Sewer Upgrade – CP#1	● On Schedule	Haren Construction continues work on schedule and within budget; July work includes E. Lyon Station Road, Joe Peed Road, and pump stations.	No action; continue monitoring schedule and budget.
I-85 Sewer Upgrade – CP#2	● On Schedule	Park Construction continues work on schedule and within budget; July work includes Central Avenue/A Street closure, railroad crossing work, and directional bore under NC Hwy. 85.	Future Board discussion on Northern Interceptor funding when scheduled.
Lead & Copper Rule	● On Schedule	Annual notices completed; service-line identification pilot remains underway.	No action; continue required compliance verifications and notifications.
Water Meter Replacement	● Schedule Modified	Creedmoor meter replacements are approximately 70% complete; revised completion target remains December 1, 2026.	Monitor revised schedule and monthly replacement progress.

South Granville Water And Sewer Authority

Executive Director's Monthly Project Update Report

July 2026

Project / Program	Status	June Update	Board Attention
Filter Media Replacement	✓ Complete	All five filters are complete; performance trends show longer run times, lower turbidity, and reduced ferric usage.	Closeout/monitoring; no Board action required.
AIA Infrastructure Assessments	● Substantially Complete	Water and wastewater final draft reports were reviewed in July; final reports are expected in August.	Closeout pending August final reports and grant deliverables.
Water Valve Replacement	● On Hold	Design is 100% complete; probable construction cost is \$710,000; project remains on hold pending 2026 public bidding with updated CIP.	Future bid timing and CIP coordination.
Water Quality Improvements	● On Schedule	Hazen & Sawyer continues hydraulic modeling, flushing program development, booster station assessments, and distribution control evaluations.	No action; monitor late-2026 deliverables.
Unidirectional Hydrant Flushing Pilot	● On Hold	Valve and hydrant exercising occurred in June; flushing was postponed due to hot weather and drought conditions, with a tentative mid-to-late September start based on Lake Holt levels.	Monitor Lake Holt levels and confirm September flushing schedule.
Water Treatment Master Plan	● On Schedule	McGill's contracted divers completed internal and external inspection of the water intake structure in mid-June.	Continue inspections, asset evaluation, and master planning toward March 2027 completion.

South Granville Water And Sewer Authority

Executive Director's Monthly Project Update Report

July 2026

Project Narratives

1) PFAS Mitigation Strategies Program

- a) **Background:** PFAS ("forever chemicals") were detected in SGWASA's source water. On April 10, 2024, EPA finalized enforceable drinking water standards for six PFAS compounds with MCLs as low as 4 ppt and introduced a Hazard Index for PFAS mixtures. SGWASA is required to complete initial PFAS monitoring by 2027, implement corrective actions by April 2029 if MCLs are exceeded, and provide public notification for violations beginning in 2029.

PFAS Treatment Options & Costs: PFAS removal can be achieved using Granular Activated Carbon (GAC), Reverse Osmosis (RO), or Ion Exchange (IX). Estimated treatment cost is \$2–\$4 per gallon per day of capacity. For SGWASA's 7.5 MGD water plant, the investment is projected at \$15–\$30 million. The current construction cost estimate for the project, at the 60% design process, is \$30.3M.

b) Summary of PFAS Compliance Action Plan

Project Progress & Schedule

- Drawings and specifications for the PFAS Advanced Water Treatment (AWT) facility met the 60% completion milestone on June 23, 2026.
- CDM Smith is now working on the plans to meet the 90% completion milestone, scheduled for September 2026.
- A distribution system corrosion control study report was completed in late June. A final report will be delivered to SGWASA by September 1, 2026.

Permitting

- Coordination is ongoing with the Town of Butner regarding special use permits and other special exemptions.
 - SGWASA and CDM Smith are scheduled to appear at the Town of Butner's August Planning Board meeting to review the permits related to the project.
- The NPDES permit renewal application is being prepared.

Funding & Financial Planning

- USDA Funding Application: Target submittal date is October 14, 2026, subject to USDA review timelines.
- Coordination with the USDA continues.
- SGWASA requested and received commercial lending terms, per the USDA's request.
- SGWASA's executive management team continues to prepare financial data for the USDA and the SGWASA Finance Committee at the September 14th meeting.

South Granville Water And Sewer Authority

Executive Director's Monthly Project Update Report

July 2026

- SRF Funding: Environmental documentation is in progress, and a Categorical Exclusion is anticipated, yet has not been received to date.
- State Appropriations: Awaiting final approval of submitted funding form.

Pilot Testing (Phase II PFAS)

- Two vendors have been selected for the expanded PFAS pilot testing project. These vendors are: AquaPRS, and Hexivon (formerly Invicta Water).
- Hexivon: Regarding their recent company changes, they will not be able to supply a pilot unit as previously scoped and discussed. They changed their business model and are no longer looking to pilot small units. They shifted to looking for longer-term, larger pilot/demonstration unit. According to Hexivon, the larger units will not be available until Q1 2027 at the earliest.
- AquaPRS: The large pilot unit was delivered to SGWASA's water treatment plant on 7/31/26. The startup and commissioning of the unit will occur in August.
 - The pilot project will operate for 90 days, targeting completion by 12/31/26.
 - Data analysis will follow with a final report expected to be provided to SGWASA staff by April 2027.
 - SGWASA staff anticipates providing a Board presentation within 30 day of receiving the final project report.

c) Funding Secured to Date:

- SGWASA received a \$5 million State Budget Grant, with approximately \$4.925 million available after administrative adjustments.
- To date, the \$4.925 grant has provided funding for a Board approved (October 2025) engineering design task order with CDM Smith in the amount of \$3,209,800. Leaving a balance of \$1,715,200.
- In March 2026, the North Carolina State Water Infrastructure Authority (SWIA) approved a total of \$10,658,880 in funding for SGWASA's \$25M-\$30M PFAS reduction water project. The award consists of a combination of loan and grant programs administered through the NC Department of Environmental Quality's Division of Water Infrastructure (NCDEQ). The summary of how much SGWASA will receive is found below:
 - \$6,658,880 in grant funding (principal forgiveness)
 - \$4,000,000 in repayable loans
- In June 2026, SGWASA was notified by the Division of Water Infrastructure that, due to a legislative correction in S.L. 2025-4, SGWASA will receive an additional \$3,000,000 in funding under S.L. 2023-134. In addition, SGWASA has been offered an additional \$500,000 in IJIA DWSRF Emerging Contaminants (EC) principal forgiveness funding.

South Granville Water And Sewer Authority Executive Director's Monthly Project Update Report July 2026

- This financial assistance package reduces the amount of long-term debt SGWASA must issue for this project and represents a substantial financial benefit to our customers while allowing us to remain on schedule to meet the EPA's April 2029 PFAS compliance deadline. Staff continues to evaluate how this confirmed loan and grant mix fits within SGWASA's overall draft funding strategy, which also includes coordination with USDA financing assistance, yet to be determined.
- **New Funding Received:** In July SGWASA received \$260,472.08 from the Aqueous Film-Forming Foam (AFFF) PFAS Multi-District Settlement (MDL 2873). The PFAS Water Settlement covers class action settlements overseen by the U.S. District Court for the District of South Carolina to compensate public water systems (PWS) for drinking water remediation costs related to "forever chemicals" (PFAS). Final approval has been granted for claims against four major manufacturers: 3M, DuPont, Tyco, and BASF.
 - In 2022, the SGWASA Executive Director and Finance Director completed the required forms to see if SGWASA qualified to be included in the class action lawsuit.
 - It appears that the compensation received from the settlement might be the only money SGWASA receives. However, SGWASA staff will continue to monitor the settlements to identify whether SGWASA will be awarded additional money.
- **Overall Status:**
 - Engineering design is underway, and the installation of PFAS Advanced Water Treatment (AWT) system is scheduled to meet the federal EPA compliance deadline. The design and construction schedule is shown below. The next Milestone relates to SGWASA receiving the 90% design for review and comments in September 2026, with final design scheduled for December 2026.

South Granville Water And Sewer Authority

Executive Director's Monthly Project Update Report

July 2026

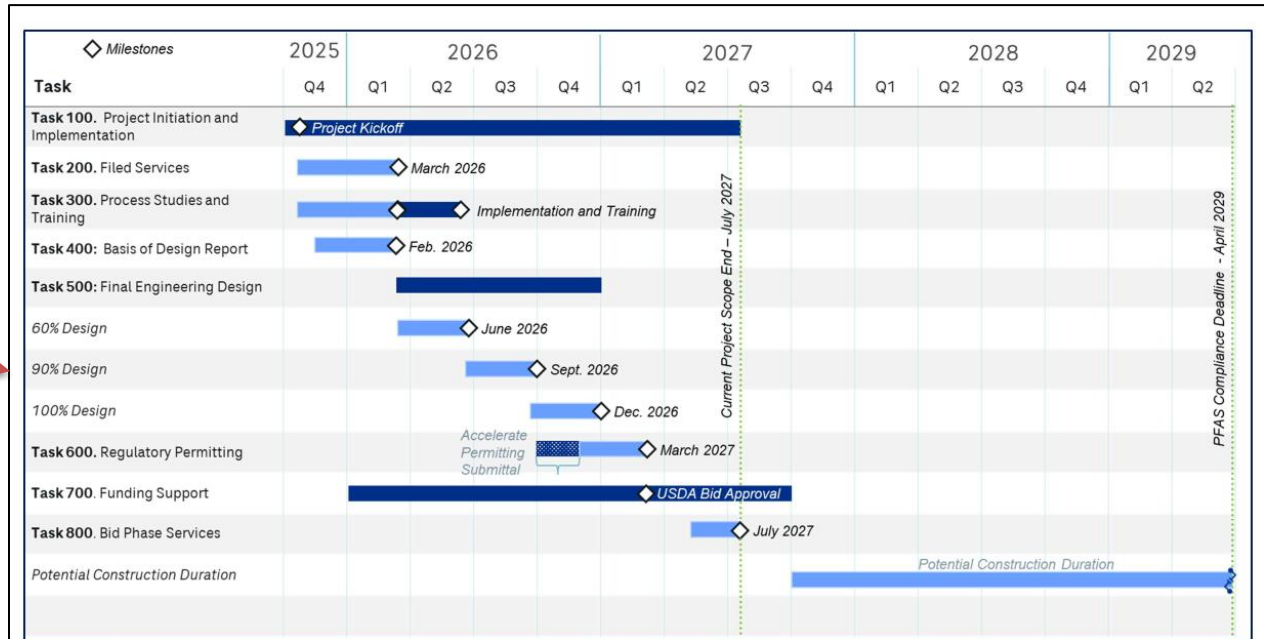


FIGURE 1: PFAS Treatment System Design and Construction Schedule

Note: The schedule was estimated from similar past projects, and ENGINEER does not control permitting or construction timelines.

South Granville Water And Sewer Authority Executive Director's Monthly Project Update Report July 2026

2) I-85 Sanitary Sewer System Improvement Project

- a) **Background:** SGWASA serves southern Granville County, including Creedmoor, Butner, and Stem. Due to maxed-out wastewater system capacity, a development moratorium was enacted in 2018 for parts of Creedmoor and Butner. From 2019–2025, SGWASA collaborated with partners to design and fund a solution. CDM-Smith completed engineering plans and split the project into two construction packages: CP#1: Bid in July 2024; contract awarded to Haren Construction for \$34.8M in December 2024. CP#2: Bid in May–June 2025. Total estimated project cost: \$75 million.

Note: Due to the proposed costs and budget constraints associated with the proposed work associated with CP#2, only the construction of the Southern Interceptor Sewer will be completed at this time. On February 27, 2026, The Finance Committee reviewed the \$8M cost for the Northern Interceptor and considered funding recommendations from staff. Further discussion is planned with the SGWASA Board of Directors at an upcoming meeting, yet to be officially scheduled.

- b) **CP#1 Status:** (In Progress/On Schedule): CP#1 includes the construction of two new sewer pump stations and the installation of new sewer pipe (gravity and force main). Haren Construction started construction on 4/1/25. Construction remains on schedule and within budget.

July's work included the following items:

- Pipe installation crossing on E. Lyon Station Rd. at E. Middleton Rd.
- Pipe installations along E. Lyon Station Rd. as well as on Joe Peed Rd.
- Construction activities at both the new Joe Peed pump station and the E. Middleton Rd. pump station.

- c) **CP#2 Status:** (In Progress/On Schedule): CP#2 includes the installation of new sewer pipe (gravity and force main), with a major pipeline crossing under I-85. Park Construction, NC, Inc. started construction on 11/1/25. Construction remains on schedule and within budget. A project timeline is shown below.


- July's work included the following items:
 - a. Central Ave. & A Street in Butner pipe installation.
 - b. Preparation for the pipe installation crossing at the Norfolk Southern railroad tracks at the northern end of A. Street.
 - c. Pipe installation activities for the directionally bored pipe under NC HWY. 85.
- 8th Street & D Street Sewer Installation Conflicts with the Gas Line:
 - a. CDM Smith, SGWASA, and Park Construction continue to work diligently with Enbridge (gas company) to resolve the issues related to the close proximity of the existing gas line and the blasting zone for the new sewer pipe installation. In

South Granville Water And Sewer Authority Executive Director's Monthly Project Update Report July 2026

summary, the blasting required to remove the granite in the project area exceeds the blasting plan tolerances originally anticipated. CDM Smith, SGWASA, and Park Construction are working on a new design for a portion of the new sewer line that may involve relocating an existing gas line and an existing water line. As of the writing of this report, CDM Smith is finalizing a design change and calculating the costs associated with this project change.

- b. 8th Street Sewer Improvement Project – Site Restoration Coordination: Staff met with the contractor to address restoration and site appearance concerns along the 8th Street project corridor. Follow-up actions include mowing overgrown areas, improving visibility at the corner of 8th and C Street by relocating project appurtenances behind the silt fence, filling potholes created during construction activities, and performing rough grading and street cleanup in completed work areas. These measures are intended to enhance site safety, improve aesthetics, and demonstrate continued responsiveness to resident concerns while construction progresses. Ongoing restoration and site maintenance activities are being monitored as construction continues.

The I-85 Sanitary Sewer Improvement Project Timeline is found below.

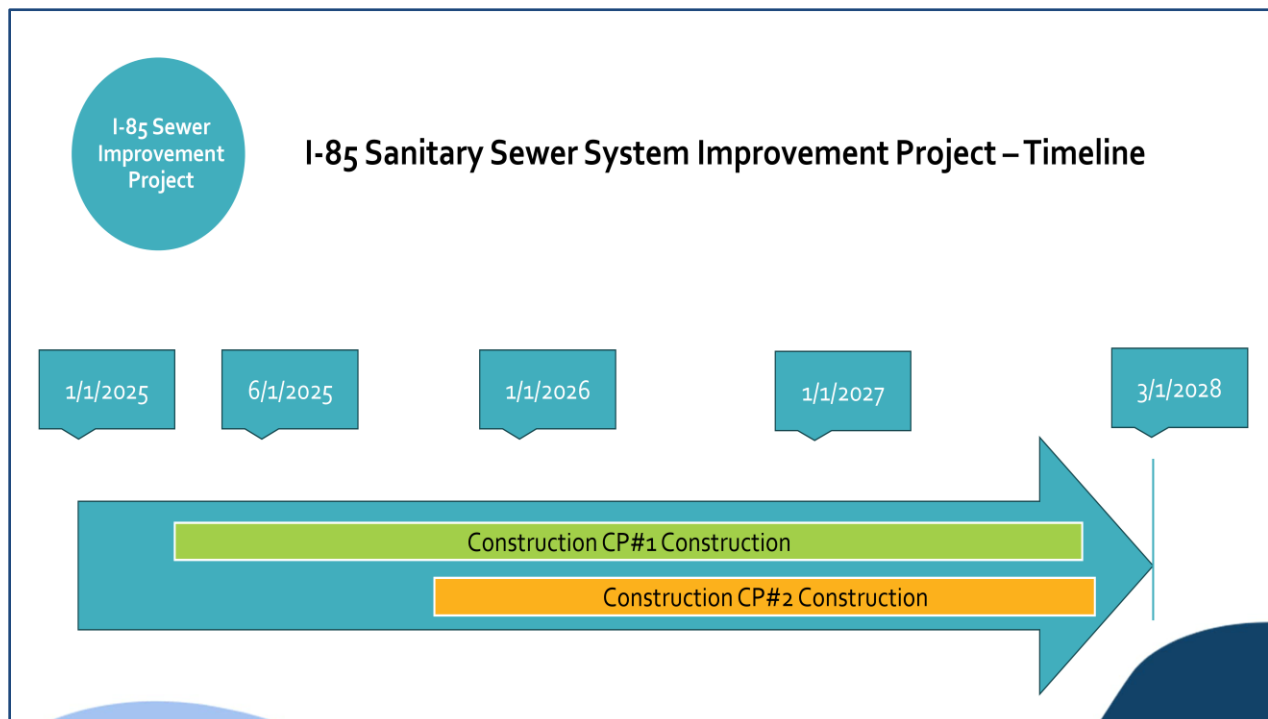

South Granville Water And Sewer Authority Executive Director's Monthly Project Update Report July 2026

3) USEPA Lead & Copper Program Update Creates Mandatory Compliance Activities for All Water Service Providers.

- a) Background:** The U.S. Environmental Protection Agency's (EPA's) Lead and Copper Rule Revisions went into effect December 16, 2021. The EPA's new Lead and Copper Rule better protects children and communities from the risks of lead exposure by better protecting children at schools and childcare facilities, getting the lead out of our nation's drinking water, and empowering communities through information. Please read more about this program below by clicking on the Fact Sheet.

EPA Lead & Copper Program [Fact Sheet](#)

- b) Status (In Progress/On Schedule):** Since 2022, SGWASA has been working with Hazen & Sawyer to manage this program. Staff is also working with a local service provider to establish a pilot program to identify service line materials.

[Click here to take the personal reporting survey.](#)

The final rule focuses on key areas that will protect our communities

 Achieving Lead Pipe Replacement Within 10 years	 Locating Legacy Lead Pipes
 Improving Tap Sampling	 Lowering the Lead Action Level to 10 µg/L
 Strengthening Protections to Reduce Exposure	 Communicating Transparently and Frequently

For more information, see <https://www.epa.gov/dwreginfo/lead-and-copper-rule>

South Granville Water And Sewer Authority Executive Director's Monthly Project Update Report July 2026

4) SGWASA - City of Creedmoor Service Area Water Meter Replacement Program

- a) **Background:** SGWASA operates about 6,600 water meters systemwide, including roughly 2,200 older meters in the Creedmoor service area that are no longer performing optimally. To improve accuracy and modernize the system, SGWASA contracted a specialized firm to replace these aging meters. This work is included in the Capital Improvement Plan (Project ID# 102-05) with a total budget of \$1,000,000.
- b) **Status (In Progress/Schedule Modified):** The water meter replacement project began in January 2026 and is expected to be completed by December 1, 2026. The contractor is replacing several hundred water meters per month. To date, approx. 70% of the water meters have been replaced.

For more information on this project, please visit

<https://www.sgwasa.org/post/creedmoor-water-meter-replacement-program>



Image: Example of the new water meter that SGWASA will be installing during this project.

South Granville Water And Sewer Authority

Executive Director's Monthly Project Update Report

July 2026

5) Water Treatment Plant Filter Analysis: Filter Media Replacement Project

- a) **Background:** In 2024, SGWASA experienced water production issues at the water treatment plant related to aging filter media and underdrain nozzles. After evaluating the system, Hazen recommended replacement of the filter media and rehabilitation of the filters to restore performance and reliability. The Board awarded the construction contract in August 2025.
- b) **Status (Complete):** The filter media and nozzle replacement project for all five filters has now been completed. The work restored critical treatment capacity and was delivered within the authorized construction budget of \$987,528. The final cost of the project was \$881,146.60. SGWASA hired Hazen professional engineers to perform water quality testing of the filter media replacement.

Water Quality Report: The filter media replacement project has been completed, and the system is fully operational. Key performance highlights to date Include:

- Filter run times have increased, indicating improved operational efficiency and longer treatment cycles.
- Treated water turbidity (see definition below) has decreased, reflecting enhanced water quality performance.
- Chemical (ferric) usage has decreased, demonstrating more effective treatment with lower demand.

Overall Impact: These measurable improvements confirm the effectiveness of the rehabilitation work and reflect the continued optimization efforts of our operations team. The system is currently operating more reliably and is better positioned to maintain regulatory compliance and deliver high-quality drinking water to our customers.

Next Steps: Staff will continue to monitor performance trends and optimize operations as needed. Additional updates will be provided as more data becomes available.

Definition(s): Turbidity is a measure of how clear or cloudy water is. What it Means in Practice

- Turbidity is caused by tiny particles suspended in the water—such as silt, clay, algae, or organic matter.
- The more particles present, the cloudier the water appears.
- Low turbidity = clear water
- High turbidity = cloudy water

This work represents SGWASA's ongoing commitment to proactive infrastructure investment, operational excellence, and the delivery of safe, high-quality water service to our community.

South Granville Water And Sewer Authority Executive Director's Monthly Project Update Report July 2026

6) AIA Grant Project for Water Infrastructure Assessment

- a) **Background:** The NCDEQ AIA Grant Program provides up to \$150,000 over three years to help utilities improve system management and asset planning. SGWASA received a \$150,000 AIA grant in 2021 for the Water Distribution System; because it was funded with ARPA dollars, no local match was required. Working with McGill Associates, SGWASA completed the grant application, scope of services, and task order. The project includes system inventory updates, master planning, hydraulic modeling, a water audit, asset management planning, CIP updates, work order system recommendations, and preparation of the final report.
- b) **Status** (Substantially Complete): SGWASA reviewed the final draft report in July. The final report will be completed in August.

7) AIA Grant Project for Wastewater Infrastructure Assessment

- a) **Background:** NCDEQ administers the AIA Grant Program to help water and wastewater utilities improve asset management and long-term financial planning. Eligible activities include asset inventories and condition assessments. SGWASA applied for the program in September 2022 and received a \$200,000 AIA grant in March 2023 for the Wastewater Collection System; because it was funded with state ARPA dollars, no local match was required. SGWASA worked with McGill Associates to prepare the grant application and develop the scope of services submitted to NCDEQ for review.
- c) **Status** (Substantially Complete): SGWASA reviewed the final draft report in July. The final report will be completed in August.

South Granville Water And Sewer Authority Executive Director's Monthly Project Update Report July 2026

8) CIP# 101-10 Water Valve Replacement Project at the Water Treatment Plant – Design & Construction

- a) **Background:** SGWASA has experienced recurring leaks and valve failures along the water main between the clear well and finished pumps, highlighting erosion issues and the need for better bypass options and system redundancy. Hazen and Sawyer is evaluating repair alternatives and preparing final design, permitting, and bid documents. The evaluation and design cost is \$155,980, with construction costs to be finalized once the preferred repair option is selected.
- b) **Status (On Hold):** Hazen & Sawyer's design work is 100% complete. The probable construction cost is \$710,000, and due to its size, the project will move to public bidding in 2026 in coordination with the updated CIP.



Images: SGWASA Water Treatment Plant – Valve Replacement Project Area.

South Granville Water And Sewer Authority Executive Director's Monthly Project Update Report July 2026

9) CIP# 102-10 Water Quality Improvements

- a) Background:** SGWASA has expressed concerns with the following items related to the water distribution network:
- The system does not currently have a hydrant flushing program to proactively help prevent water quality issues.
 - Water quality and chlorine residual issues at booster stations throughout the distribution system.
 - The lack of water tower control within the distribution system.

For this project, Hazen and Sawyer will be conducting a preliminary investigation and will perform the following tasks:

- Data collection and data review.
- Water hydraulic model update and calibration
- Developing hydraulic model simulations of water age in the distribution system.
- Developing a hydrant flushing program.
- Performing assessments of the water booster pump stations.
- Evaluating the water distribution system control network and then developing improvements based on the data.

Project deliverables include:

- Unidirectional Hydrant Flushing Program (see more information on this project below)
- Draft and Final Booster Pump Station Assessment TM
- Draft and Final Distribution System Control Assessment TM
- Updated hydraulic model

The total cost for the project is \$227,340.00.

- b) Status (In Progress/On Schedule):** This project is being performed by Hazen & Sawyer. The project was initiated in the fall of 2024. The goal is to complete this project in late 2026.

South Granville Water And Sewer Authority Executive Director's Monthly Project Update Report July 2026

10) Unidirectional Hydrant Flushing Pilot Project – City of Creedmoor SGWASA Service Area

- a) **Background:** SGWASA has developed a pilot unidirectional flushing program in the Golden Pond subdivision in Creedmoor to improve water quality and system operations. The pilot covers about 5.3 miles of water main and includes model updates, a flushing plan, field support, and customer communication. The \$45,000 cost is funded through the FY 2025–2026 engineering projects budget.
- b) **Status (On Hold):** Utility crews performed valve and hydrant exercising in June. Due to hot weather and localized drought conditions, the June flushing schedule was postponed. SGWASA continues to monitor the water level at Lake Holt to determine when the scheduled flushing can occur. Based on July month-end rainfall amounts and the water level increasing at Lake Holt, SGWASA will tentatively schedule the unidirectional flushing program to begin in mid to late September.

11) CIP# 101-01 Water Treatment Master Plan: AIA Grant Funded

- a) **Background:** SGWASA was awarded a \$150,000 NCDEQ grant to complete a Water Treatment Plant Master Plan and is partnering with McGill Associates. SGWASA will provide the required 20% match (\$30,000). The project includes updating asset inventories, evaluating critical infrastructure condition, and advancing long-term asset management planning.
- b) **Status (In Progress/On Schedule):** The Board approved grant acceptance in October 2025 and the McGill task order in November 2025. The project began in December 2025. As a part of this project, in mid-June, underwater divers, contracted by McGill Associates, completed the internal and external inspection of the water intake structure. This inspection was just one of the many infrastructure inspections being performed as a part of this project. The project is scheduled for completion in March 2027.

South Granville Water And Sewer Authority

Executive Director's Monthly Project Update Report

July 2026

Board Actions (Past 90 Days)

Board Meeting Month/Year	Topic	Status
May 2026	National Public Works Week Proclamation	The Board approved this item.
May 2026	Proposed FY2026-27 Budget Review	The Board approved the FY2026-27 Budget
May 2026	Write off of Accounts Receivable	The Board approved this item.
May 2026	FY2025-26 3rd Quarter Financial Review	The Board approved this item.
June 2026	SGWASA I-85 Sanitary Sewer Improvement Project Update Presentation	No Board action required.
June 2026	FY2025-26 Year-End Auditing Services – Award of Contract	The Board approved this item.
June 2026	Fiscal Year 2025-2026 4th Quarter Internally Approved Budget Amendments & Fiscal Year 2025-2026 Budget Amendment #13	The Board approved this item.
June 2026	Position Classification Plan Update Based on Approved FY2026-27 Budget	The Board approved this item.
June 2026	SGWASA Employee Benefits - Contract Renewals for FY2026-27	The Board approved this item.
July 2026	Check and Purchase Order Countersigning Authority Resolution – Revision	The Board approved this item.
July 2026	Amendment of Capital Reserve Fund For System Development Fees	The Board approved this item.
July 2026	FY2025-26 Fiscal Year-End Capital Improvement Project Fund Designation	The Board approved this item.

South Granville Water And Sewer Authority

Executive Director's Monthly Project Update Report

July 2026

Utility Operations Highlights

Water Distribution System Topics

- 1) None.

Wastewater Collection System Topics

- 1) Sanitary Sewer Overflows (SSO's):
 - a) None.
- 2) Other Topics: None

Water Treatment Plant Topics

- 1) None.

Wastewater Treatment Plant Topics

- 1) None.

Utility Customer Service/Administration Topics

- 1) No operating issues.

South Granville Water And Sewer Authority Executive Director's Monthly Project Update Report July 2026

Staffing Summary

The FY2026-27 Budget authorized 53 full-time employees. The current staffing level is above 94%.

The following is a breakdown of the status of several vacancies.

Vacant Positions – Currently Advertising and/or Interviewing

Billing Customer Service Supervisor (1)

Vacant Positions – Final Candidate Selected/Pending Background Checks

None

Recent New Hires

None

Recent Internal Promotions

None

(End of Report)
